Rolling Stock Maintenance and Reliability Report

Kochi Metro Rail Limited · Rolling Stock Division, Muttom Depot
Report no. KMRL/RS/MR/2025-Q2/07 · Quarter: July to September 2025 (Q2 FY 2025-26)
Prepared by: Rolling Stock Maintenance Section · Issued: 8 October 2025

1. Summary


This report covers maintenance of the 25 three-car Alstom Metropolis trainsets operated on the Aluva to Thrippunithura line during Q2 FY 2025-26. Fleet availability averaged 96.4 percent against a target of 95 percent. Mean Distance Between Failures (MDBF) fell below target in August 2025 because of two brake caliper faults, and recovered to 44,900 km in September 2025.

Two trainsets, TS-07 and TS-11, are due for their 4-year bogie overhaul. The overhaul must be completed before 30 November 2025. Spare wheelsets for the overhaul were received under work order WO-RS-2025-0412.

2. Fleet key figures


Indicator	Jul 2025	Aug 2025	Sep 2025	Target
Fleet availability	96.8%	95.1%	97.2%	95.0%
MDBF (km)	41,200	38,600	44,900	40,000
Service-affecting failures	3	5	2	<= 4
Planned maintenance done	100%	98%	100%	100%

Figure 1 shows MDBF by month against the 40,000 km target.

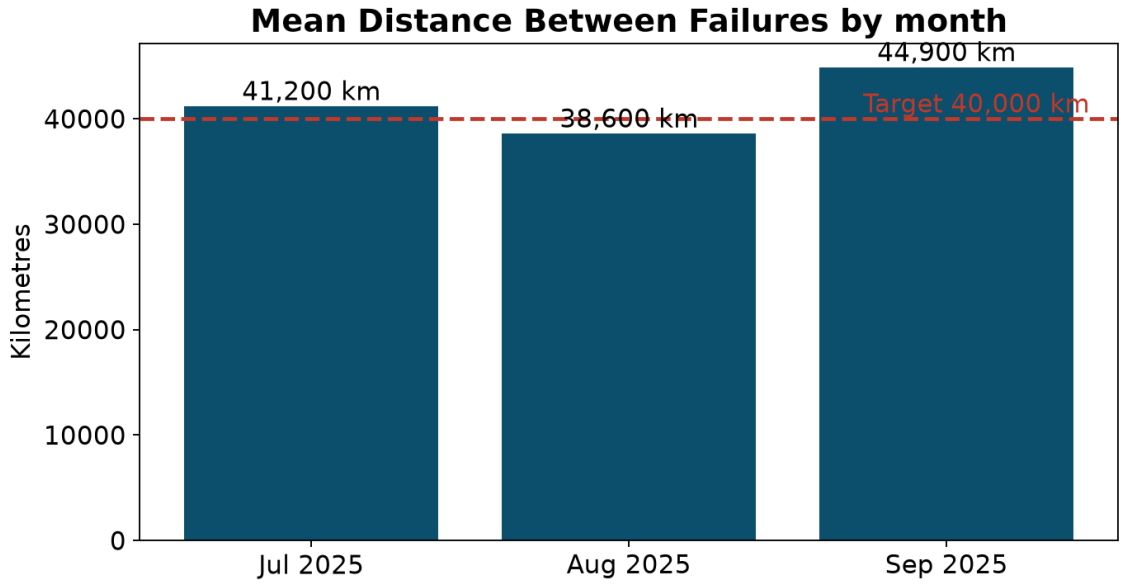

3. Maintenance workflow

Figure 2 shows how a trainset moves through the depot. Faults found in the daily A-check are logged in the Maintenance Management System (MMS) and closed only after quality sign-off.

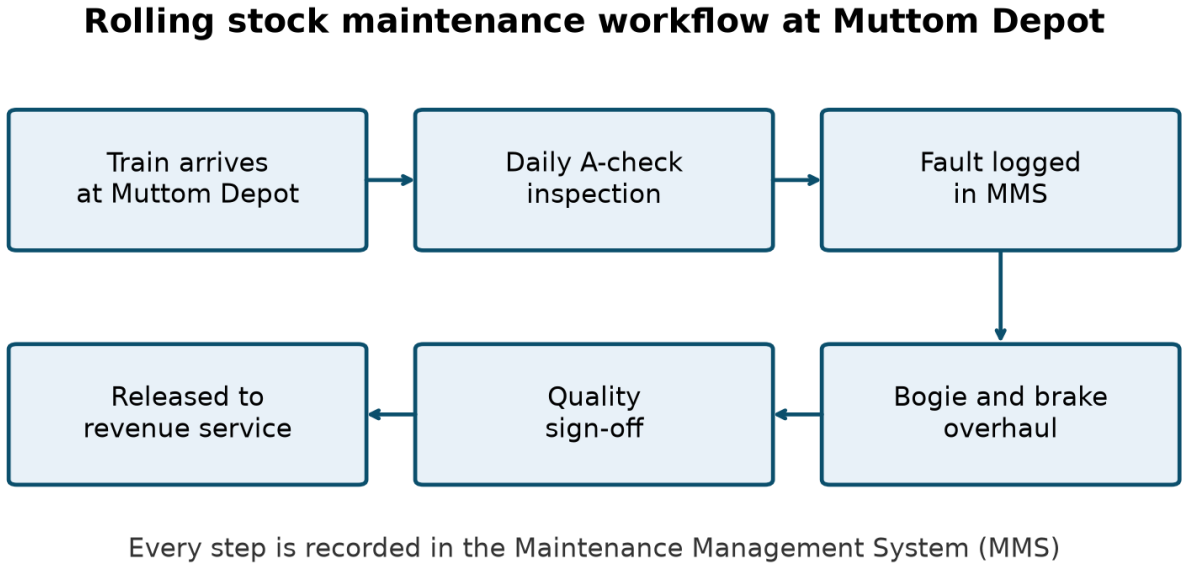

4. Findings

4.1 Brake calipers: two caliper seal failures on TS-04 and TS-15 in August 2025 caused the MDBF dip. Seals from the same batch were replaced on all trainsets by 12 September 2025.

4.2 Air-conditioning: saloon AC units met the cooling specification on all trainsets; filters are now cleaned every 15 days during the monsoon instead of every 30 days.

4.3 Wheel profile: wheel turning on the under-floor lathe was done for 6 trainsets; all are within the flange thickness limit.

5. Action items

Action	Owner	Due
Complete bogie overhaul of TS-07 and TS-11	Rolling Stock Maintenance	30 Nov 2025
Audit brake caliper seal batch with supplier	Rolling Stock Maintenance	15 Nov 2025
Share AC filter interval change with Operations	Depot Manager, Muttom	20 Oct 2025
Plan Q3 wheel turning for remaining trainsets	Rolling Stock Maintenance	31 Dec 2025

The signed approval note is attached as the last page (scanned copy).

KOCHI METRO RAIL LIMITED

Muttom Depot - Rolling Stock Division

APPROVAL NOTE

Report: KMRL/RS/MR/2025-Q2/07

The quarterly maintenance and reliability report for July to September 2025 is approved for circulation to Operations and Safety.

Bogie overhaul of trainsets TS-07 and TS-11 to be completed before 30 November 2025.

Approved by: Depot Manager, Muttom

Date: 10 October 2025
